

VILLAGE OF EAST AURORA
716-652-6057 DPW

Department of Public Works
Application for Storm Sewer Connection

Application Fee \$25.00

Date _____

Receipt # _____

Permit Fee – Storm Sewer Connection \$200.00

I/We _____, hereby make application for:
Class _____ Storm Sewer Connection to be installed at
_____ under the supervision of an authorized agent of the Village of East
Aurora at a cost of \$_____.

I/We agree that all piping between the street line and structure to be of Cast Iron, Concrete Sewer Pipe, or PVC Schedule 35 or equal having a wall thickness of .120" for 4", integral gasket type, bedded in at least 6" of select fill.

That: All pipes will be cast iron coming through foundation up to and including the 1st cleanout & trap.

That: All traps and cleanouts must be a minimum of 10' (ten feet) from foundation.

That: Sewer pipe shall be located no less than 2' (two feet) from water service pipe.

That: an authorized agent of the Village must inspect Sewer piping, before the pipe is covered, or trench filled.

That: The Building Inspector and the Public Works Department must be notified when installation is ready for inspection. (Inspections to be made between 8:00 A.M. and 3:00 P.M.)

Pipe shall be placed on a full trench width (minimum width 12" wider than pipe) 6" thick bedding of stone.

Stone backfill shall be placed full trench width from stone bedding for a minimum of 6" depth over pipe.

Stone shall be 3/8" crushed limestone or washed crushed gravel of equal size.

Connections to Village Line are to be a FURNCO coupling or Pipe Manufacturers Adaptor.

Date: _____

(Signature of Applicant)

Tap Made: _____

Service Line Inspected & Found Satisfactory

By: _____

Date: _____

Application for Storm Sewer Service Disconnection

Date: _____

Pd. _____

Application Fee: \$25.00

Permit Fee: \$200.000

Receipt # _____

(Clerk's Office)


I/We _____, owners of the property
at _____, East Aurora, New York, hereby apply to the Village of East Aurora
for disconnection of storm sewer service line at the above address. The building is planned for demolition,
which is to commence on _____ 20____. (Allow one-week time from filing of this application.)

All storm sewer disconnects shall be made by the owner's contractor. Once completed, the disconnect shall be inspected jointly by the Department of Public Works and Erie County Sewer District. Please call the Department of Public Works @ 652-6057 to schedule inspection.

(Signature of Owner)


Service Disconnect Inspected & Found Satisfactory by: _____

Date of Inspection: _____

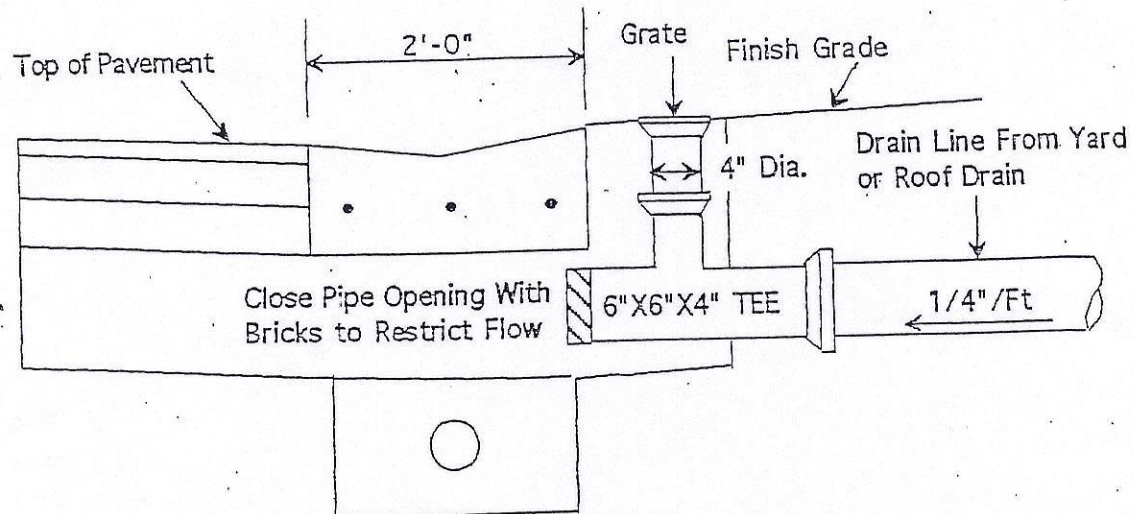

TYPICAL CURB BUBBLER CONCRETE GUTTER CBCG-1

Scale $3/4" = 1'$

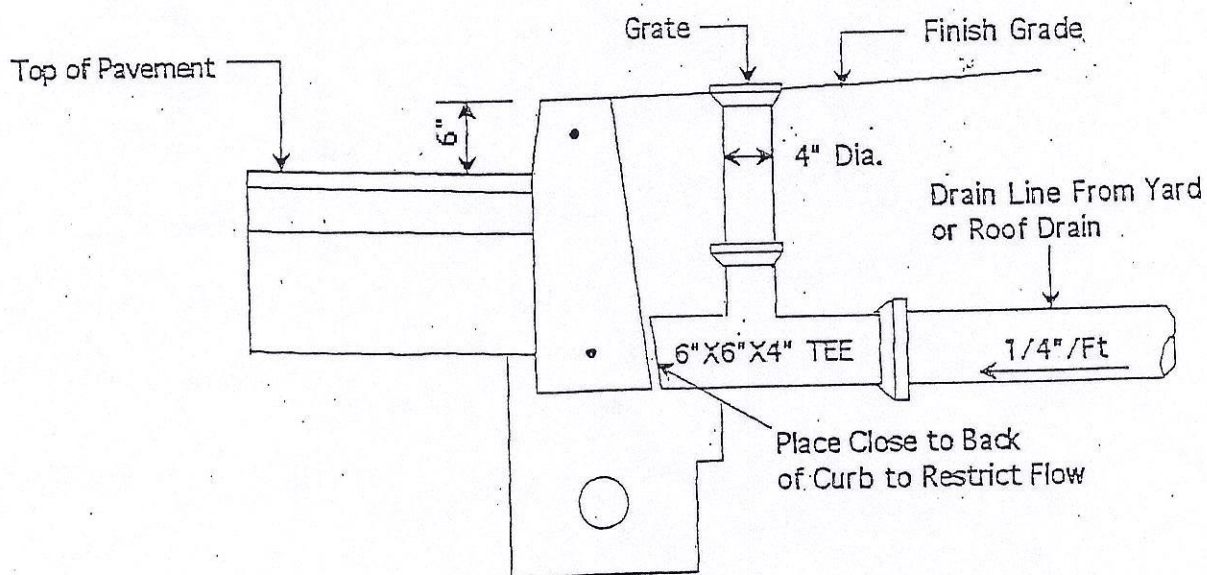

TYPICAL CURB BUBBLER UPRIGHT CURB CBUC-1

Scale $3/4" = 1'$
