

CITY OF GLOVERSVILLE  
DEPARTMENT OF PUBLIC WORKS  
SIDEWALK, CURB CUT, DRIVEWAY & APRON PERMIT  
**\$30 fee due upon completion of application**

NO: \_\_\_\_\_

DATE: \_\_\_\_\_

PERMISSION IS HEREBY GIVEN:

\_\_\_\_\_  
Contractor's Name

\_\_\_\_\_  
Telephone

\_\_\_\_\_  
Property Owner's Name

\_\_\_\_\_  
Telephone

TO EXCAVATE FOR AND CONSTRUCT SIDEWALK, CURB OR OTHER SIDEWALK/DRIVEWAY

CONSTRUCTION AT \_\_\_\_\_

PROPERTY ADDRESS

DESCRIBE TYPE OF WORK AND MATERIALS \_\_\_\_\_

\_\_\_\_\_  
ATTENTION: PRIOR TO INSTALLATION OF REPLACEMENT MATERIALS, AN INSPECTION  
IS REQUIRED TO EVALUATE CONFORMANCE WITH OUTLINED SPECIFICATIONS (ON REVERSE)  
PLEASE CALL THE PUBLIC WORKS OFFICE TO ARRANGE AN APPOINTMENT FOR  
INSPECTION AT 518-773-4556

\_\_\_\_\_  
AUTHORIZED PERSONNEL

\_\_\_\_\_  
INSPECTOR

\_\_\_\_\_  
PERMIT ISSUANCE DATE

\_\_\_\_\_  
INSPECTION DATE

- A 72 HOUR NOTICE IS REQUIRED AFTER SUBMISSION OF APPLICATION FOR PRE INSTALLATION INSPECTION
- ONCE WORK IS COMPLETE, A POST CONSTRUCTION INSPECTION IS REQUIRED TO VERIFY COMPLIANCE
- PERMIT IS VALID FOR ONE YEAR FROM DATE OF ISSUE

Fee Received By: \_\_\_\_\_ (clerk/deputy)      Date: \_\_\_\_\_

# SPECIFICATION OUTLINE

## FOR SIDEWALK REPLACEMENT, DRIVEWAY INSTALLATION AND/OR CURB CUT

### SIDEWALKS:

All new sidewalks, including the replacement of any portion of existing sidewalks, shall be comprised of concrete

4" thick

6" thick at driveways

Should be divided into 4' or 5' squares depending on sidewalk width

Place an expansion joint every 15' or 20'

Place an expansion joint at driveways, driveway aprons or abutting walks

Grade should follow curb line but should slope 1/2" drop per foot

Recommend 3,000 PSI concrete, air entrained mix

Reinforcing mesh not required, but recommended. If used, place near middle of thickness, break mesh at expansion joints

Width - match existing sidewalks on adjacent properties, if not a replacement of an existing walk

Location - house or property side edge should be on street right of way line

Corner lots - remove curbing and install handicap curb ramps in accordance with ANSI A117.1-1986 Section 4.7

### CURBS:

Curb Installation - curb shall be constructed in maximum 20' long segments with construction joints and to the grade of existing street, matching existing reveal

If no curbs presently - reveal to be 6"

Minimum width of curb 6"

Alternately pre-cast concrete or granite stone curbing may be used as approved by the City Engineer or Director of Public Works


### DRIVEWAYS:

For new installations with a minimum base course of 6", a minimum of 3" surface course of hot mix asphalt or a 6" minimum course of portland cement may be installed

If resurfacing existing asphalt driveway, a minimum of 1 1/2" of hot mix asphalt may be used.

All new sidewalks, including the replacement of any portion of existing sidewalks, shall be comprised of concrete. No other materials are authorized for the composition of any new sidewalk.

For all portions of any new sidewalk or replacement sidewalk within the boundary of any driveway, the minimum depth of concrete shall be six inches.

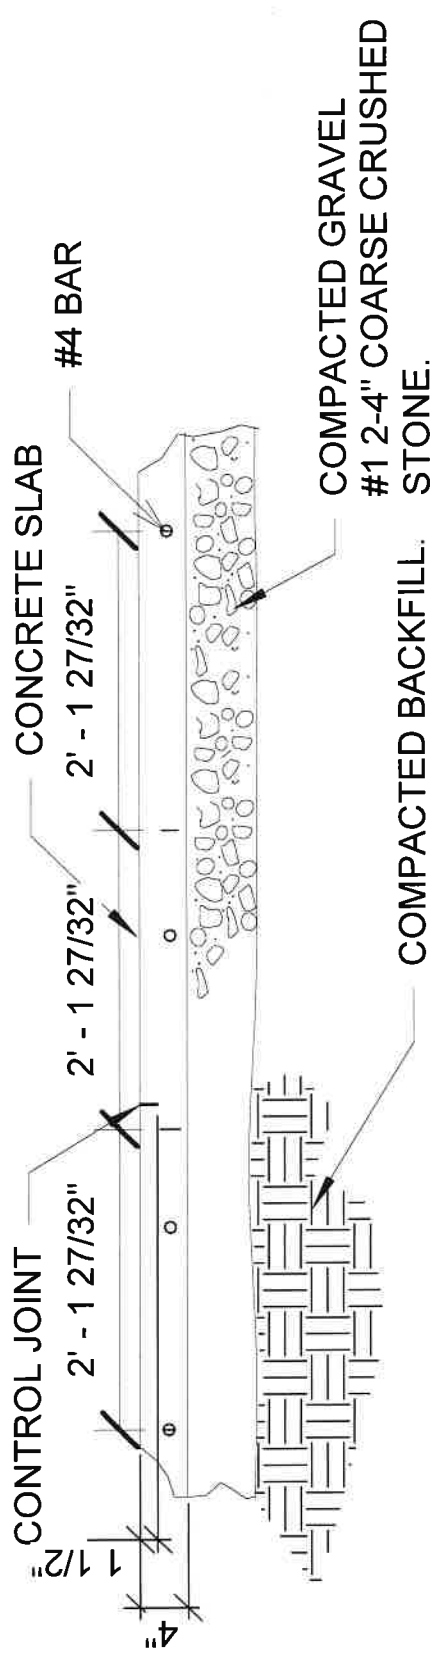

#### NOTES:

1. DOWEL IS TYPICAL AT ALL EJs EXCEPT AGAINST VERTICAL JOINTS WITH WALLS, CURBS OR SITE IMPROVEMENTS.
2. TOOLED EDGES AND JOINTS. ALL PANELS.
3. INSTALL CONTROL JOINTS MAX. 5'
