



CITY OF MENIFEE
MEMORANDUM

NOTIFICATION OF ACCEPTANCE OF PUBLIC IMPROVEMENTS

Community Services Department

DATE:

ATTENTION:

THE FOLLOWING IMPROVEMENTS HAVE BEEN ACCEPTED AS COMPLETE TO CITY SPECIFICATIONS AND SHOULD NOW BE INCLUDED IN THE CITY OF MENIFEE FIXED ASSET REPORT INVENTORY AND MAINTENANCE INVENTORY

PROJECT				
Location				
Special Districts				
Council Date				
DEPARTMENT	FACILITY ACCEPTED	QTY/UNIT	LOCATION OR ATTACHED EXHIBIT	FUNDING
Community Services	ROW Landscaping	SF		
	Monument/Sign	EA		
	Fuel Mod with Irrigation	SF		
	Fuel Mod W/O Irrigation	SF		
	DG Trail	SF		
		LF		
	ROW Trail Fencing	LF		
	Community Park	SF		
	Community Building Facility	SF		
	Sports Field/Court	SF		
	Sports Field Lighting	EA		
	Restroom	SF		
	Playground	SF		
ESTIMATED COST OF IMPROVEMENTS:				
FACILITY		COST		
Street and Drainage				
Water System and Sewer System (EMWD)				

UTILITY TYPE	METER ADDRESS	METER #


Please update your inventory and records, if you have any questions please contact the Community Services Department at (951) 723-3752 ask for Bryce Howell.

Prepared By:	Date:
Approved By:	Date:

*HIGHLIGHTED CELLS TO COMPLETED BY APPLICANT

DEVELOPER TO SUBMIT EXHIBIT IDENTIFYING
LOCATION ALL IMPROVEMENTS LISTED ON
ACCEPTANCE FORM

EXAMPLE
PUBLIC IMPROVMENTS FOR AUDIE
MURPHY RANCH TM 36484

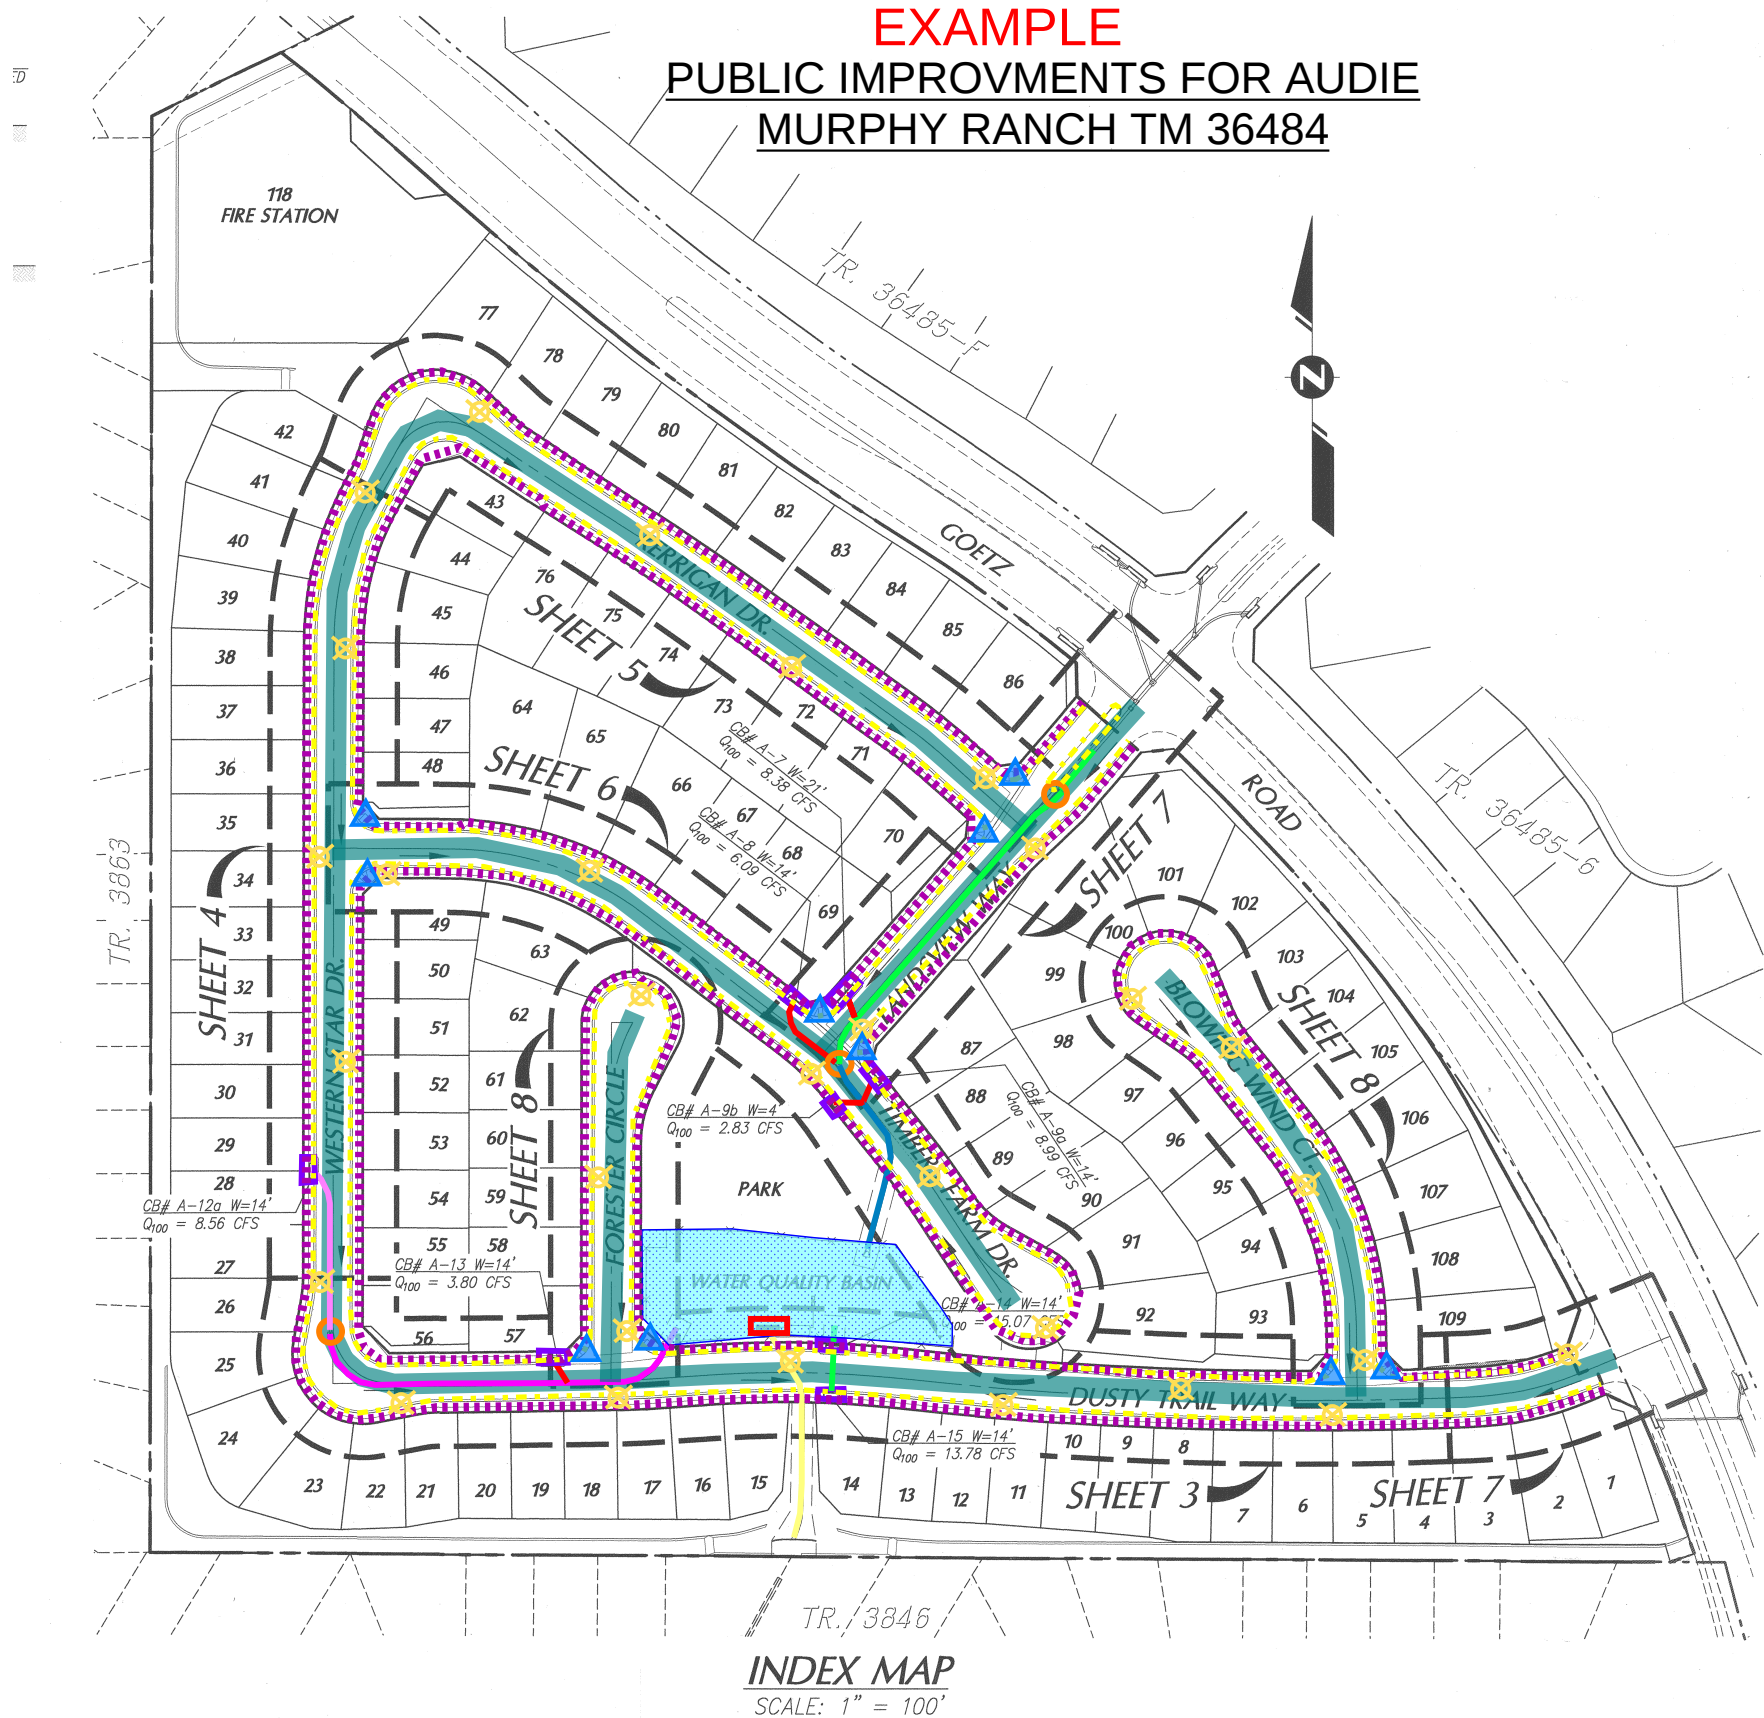

LEGEND

CONSTRUCTION NOTES		QTY	UNIT
1	CONSTRUCT 4" AC OVER 6" AB CL II PER TYPICAL SECTION OF SHEET 2	168,110	SF
2	CONSTRUCT TYPE 6 AND GUTTER PER CITY OF MENIFEE STD. PLAN NO. 200	9,210	LF
3	CONSTRUCT TYPE 8A CURB PER CITY OF MENIFEE STD. PLAN NO. 203	170	LF
4	CONSTRUCT CONCRETE SIDEWALK PER CITY OF MENIFEE STD. PLAN NO. 400, MODIFIED PER DETAIL ON SHEET 2	33,260	SF
4A	CONSTRUCT CURB ADJACENT SIDEWALK PER CITY OF MENIFEE STD. PLAN NO. 400	14,230	SF
20	INSTALL 18" RCP (D LOAD PER PROFILE)	210	LF
21	INSTALL 24" RCP (D LOAD PER PROFILE)	680	LF
22	INSTALL 30" RCP (D LOAD PER PROFILE)	390	LF
23	INSTALL 36" RCP (D LOAD PER PROFILE)	195	LF
24	INSTALL 42" RCP (D LOAD PER PROFILE)	200	LF
26	CONSTRUCT CURB INLET CATCH BASIN PER RIVERSIDE COUNTY STD. PLAN NO. 300 WITH TRASH CAPTURE DEVICE PER CITY APPROVED LIST	8	EA
27	CONSTRUCT MANHOLE NO. 1 PER R.C.F.C. & W.C.D. STD. DWG. NO. MH251	2	EA
28	CONSTRUCT MANHOLE NO. 4 PER R.C.F.C. & W.C.D. STD. DWG. NO. MH254	1	EA
38	CONSTRUCT BASIN OUTLET STRUCTURE PER DETAIL ON SHEET 14	1	EA
INSTALL STREET LIGHT		31	EA
WQMP BASIN		1	EA
CURB RAMP		10	EA

EXHIBIT SHALL INCLUDE LEGEND WITH
QUANTITIES FOR PUBLIC
IMPROVEMENTS TO BE ACCEPTED BY
CITY COUNCIL
